P3O

Portfolio, Programme and Project Offices Framework

Joao Luiz D'Andrea

Table of contents

1 Overview **2**
- 1.1 What is P3O . . . 2
- 1.2 Purpose . . . 3
- 1.3 When to Use It . . . 3
- 1.4 Target Audience . . . 3
- 1.5 P3O Operating Model Overview . . . 4

2 History and Evolution **5**

3 Core Principles **6**

4 Governance Structure **6**
- 4.1 What P3O Governs . . . 6
- 4.2 Common P3O Components . . . 7
- 4.3 Key Roles . . . 7
- 4.4 P3O Service Areas . . . 8

5 P3O Model Design **8**
- 5.1 Permanent and Temporary Offices . . . 8
- 5.2 Hub-and-Spoke Pattern . . . 9
- 5.3 Service Catalogue Thinking . . . 9

6 Lifecycle and Implementation Approach **9**
- 6.1 Typical Implementation Stages . . . 9
- 6.2 Example Implementation Flow . . . 10

7 Artefacts and Documentation **10**
- 7.1 Example Document Grouping . . . 11
  - 7.1.1 Strategic / Enterprise Level . . . 11

7.1.2 Programme / Delivery Level 11
7.1.3 Project / Local Support Level 11

8 RACI Matrix **12**

9 Integration with Other Frameworks **13**
9.1 P3O and COBIT 13
9.2 P3O and MoP 14
9.3 P3O and MSP 14
9.4 P3O and PRINCE2 14
9.5 P3O and ITIL 4 14
9.6 P3O and TOGAF 14

10 KPIs and Measures **14**

11 Benefits **15**

12 Limitations and Risks **15**

13 Practical Use Case **16**

14 Conclusion **16**

15 References **17**

1 Overview

1.1 What is P3O

P3O stands for **Portfolio, Programme and Project Offices**. It is a framework for designing, implementing, and operating a coordinated office model that supports strategic change across the enterprise. Rather than defining a single PMO shape, P3O explains how different support offices can be organised and linked so that portfolio decisions, programme coordination, and project control work as one governance system.

P3O helps organisations move beyond isolated project administration. It creates an operating model in which decision support, assurance, standards, reporting, resource coordination, benefits tracking, and delivery enablement are aligned across change initiatives.

In current official positioning, P3O remains part of the wider PeopleCert / AXELOS family of portfolio, programme, and project management guidance. The current certification path is presented as **P3O Foundation** and **P3O Practitioner**.

1.2 Purpose

The purpose of P3O is to help organisations:

- create a coherent office model for change governance;
- define how portfolio, programme, and project support functions should fit together;
- improve visibility, consistency, standards, and decision support;
- strengthen prioritisation, dependency management, and reporting;
- provide executive information for investment and assurance decisions; and
- make PMOs more strategic, value-adding, and scalable.

1.3 When to Use It


P3O is especially useful when an organisation has many concurrent initiatives and needs more than a single local PMO. Typical situations include:

- enterprise transformation with multiple programmes and projects;
- organisations building or redesigning a PMO operating model;
- environments with weak visibility across the change portfolio;
- delivery landscapes with inconsistent methods, templates, and reporting;
- organisations needing clearer assurance, governance, and escalation routes;
- complex change involving shared resources and cross-project dependencies; and
- public sector, regulated, or board-driven environments where structured reporting and control matter.

1.4 Target Audience

- Portfolio Directors / Heads of Change
- PMO Leaders / EPMO Leaders
- Programme Directors and Programme Managers
- Project Managers and Delivery Managers
- Transformation Office leaders
- CIO / COO / Change Steering Boards
- Governance, assurance, audit, and risk teams
- Resource and capacity managers
- Benefits and business change managers
- Executives needing enterprise delivery insight

1.5 P3O Operating Model Overview

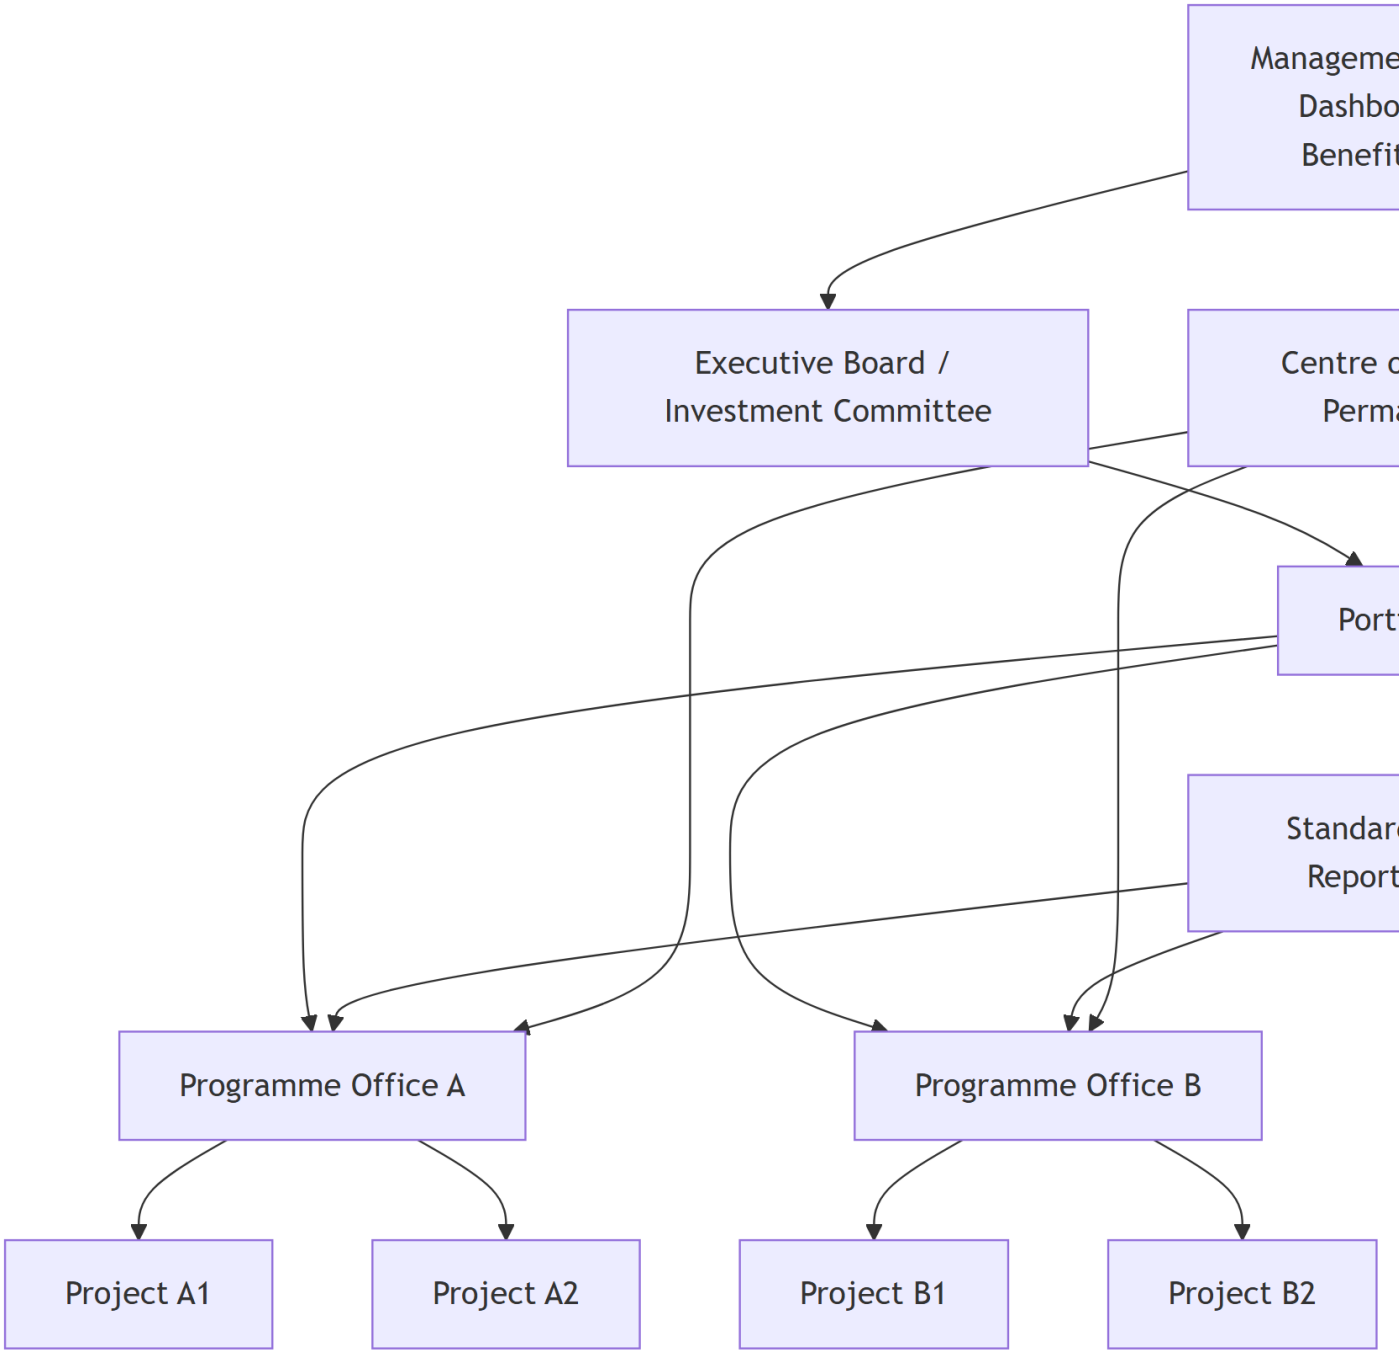

P3O treats support offices as an integrated system rather than isolated admin units. A mature model may contain a **permanent portfolio office**, temporary or permanent **programme**

offices, local **project offices**, and a **centre of excellence** that sets standards and develops capability.

---

2 History and Evolution

Version / Milestone	Year	Key Changes
Early PMO practice	1990s–2000s	Organisations establish project offices with inconsistent roles and scope
P3O guidance first established	2008–2013 era	Formalised a structured office model linking portfolio, programme, and project support
AXELOS era	2013 onward	P3O positioned with PRINCE2, MSP, and MoP as part of integrated change governance
PeopleCert stewardship	2021 onward	Continued official certification and positioning under the wider best-practice portfolio
Current official certification path	Current	P3O Foundation and P3O Practitioner remain the main formal route

P3O emerged to solve a recurring organisational problem: PMOs often evolved locally and tactically, which created duplication, inconsistent reporting, unclear authority, and poor enterprise visibility. The framework reframed the PMO as a **network of offices and services** that can be centrally governed yet locally tailored.

It is best understood not as a delivery method like PRINCE2, but as an **organisational design framework** for how change support functions should be structured and governed.

---

3 Core Principles

P3O is commonly explained through a set of design and operating principles. Even where organisations tailor the framework, these ideas remain central.

1. **Align the office model to organisational strategy**
   The office structure must support how the organisation prioritises, authorises, funds, and governs change.
2. **Differentiate portfolio, programme, and project needs**
   A portfolio office serves enterprise prioritisation and oversight; programme and project offices support delivery at different levels of detail.
3. **Provide decision-enabling information**
   Reporting should support governance decisions, not just produce status documents.
4. **Standardise where valuable, tailor where necessary**
   Templates, controls, definitions, and reporting should be consistent, but scaled to context.
5. **Support delivery, not bureaucracy**
   A P3O should remove friction, improve transparency, and enable better outcomes rather than become an administrative burden.
6. **Build capability and continuous improvement**
   The office model should coach, assure, analyse, and mature delivery practices over time.
7. **Clarify services, roles, and accountabilities**
   Each office component should have a defined service catalogue, authority, interfaces, and customer base.

---

4 Governance Structure

4.1 What P3O Governs

P3O governs the **support system around change**, including:

- delivery reporting and management information;
- governance calendars, reviews, and control points;
- standards, methods, templates, and guidance;
- RAID, dependency, and issue escalation coordination;
- financial tracking and portfolio-level visibility;
- resource and capacity insight;

- assurance coordination and health checks; and
- benefits tracking and decision support.

4.2 Common P3O Components

P3O Component	Main Purpose
Portfolio Office	Supports enterprise prioritisation, investment governance, portfolio reporting, and strategic control
Programme Office	Supports a specific programme with planning, control, dependency, benefits, and governance support
Project Office	Supports one or more projects with local control, scheduling, reporting, RAID, and admin services
Centre of Excellence	Defines standards, methods, capability development, coaching, tools, and assurance approaches
Temporary Office	Created for a specific initiative or lifecycle phase
Permanent Office	Provides ongoing enterprise support capability and institutional memory

4.3 Key Roles

Role	Main Accountability
Portfolio Director / Head of Change	Owns enterprise change visibility and prioritisation support
P3O Sponsor	Provides executive backing, funding, and mandate
Head of P3O / EPMO Lead	Designs and runs the integrated office model
Portfolio Analyst	Supports prioritisation, dashboards, financial and dependency insight
Programme Office Manager	Runs office services for a programme and supports governance
Project Office Manager / PMO Lead	Supports project controls, reporting, and administration
Centre of Excellence Lead	Owns methods, templates, maturity, training, and standards

Role	Main Accountability
Assurance Lead	Coordinates reviews, health checks, and governance confidence
Resource / Capacity Manager	Provides resource planning and utilisation insight
Benefits / Business Change Analyst	Tracks value, outcomes, and benefit realisation support

4.4 P3O Service Areas

Typical P3O services include:

- governance and control support;
- management information and dashboards;
- planning and schedule coordination;
- RAID and dependency management;
- resource and capacity reporting;
- financial and portfolio analysis;
- benefits and outcomes tracking;
- standards, methods, templates, and tools;
- assurance coordination; and
- coaching, onboarding, and capability development.

---

5 P3O Model Design

5.1 Permanent and Temporary Offices

P3O distinguishes between **permanent offices** and **temporary offices**.

- **Permanent offices** provide enduring organisational capability, standards, governance support, and enterprise memory.
- **Temporary offices** are created for a programme or major project for the duration of that initiative.

A mature enterprise often uses a hybrid design: a permanent portfolio office and centre of excellence, with temporary or semi-permanent programme/project support offices created as needed.

5.2 Hub-and-Spoke Pattern

A common P3O design is a **hub-and-spoke model**:

- the **hub** provides governance standards, tools, data definitions, capability development, and consolidated reporting; and
- the **spokes** provide local support embedded within programmes or projects.

This balances consistency and proximity to delivery teams.

5.3 Service Catalogue Thinking

One of the most practical ways to implement P3O is to define the office as a set of services rather than only an organisation chart. Example service groups:

- governance support;
- reporting and analytics;
- planning and controls;
- financial administration and analysis;
- risk / issue / dependency coordination;
- benefits tracking;
- assurance support; and
- method and capability support.

---

6 Lifecycle and Implementation Approach

P3O is not a delivery lifecycle like PRINCE2 or MSP. It is better implemented through a staged capability design and rollout.

6.1 Typical Implementation Stages

Stage	Purpose	Typical Outputs
Assess Current State	Understand existing PMOs, pain points, and governance gaps	Maturity assessment, service inventory, stakeholder map
Define Vision and Scope	Clarify the target P3O model and expected value	P3O vision, business case, target operating model

Stage	Purpose	Typical Outputs
Design the Model	Define structures, services, roles, tools, and interfaces	Organisation design, service catalogue, RACI, process maps
Pilot / Mobilise	Trial the model in selected areas	Pilot office, dashboards, templates, lessons learned
Implement at Scale	Roll out across the enterprise	Governance calendar, reporting standards, consolidated MI
Improve and Mature	Refine services and capability	KPIs, maturity reviews, continuous improvement backlog

6.2 Example Implementation Flow



---

7 Artefacts and Documentation

P3O is highly document- and data-oriented. The exact outputs vary by design, but common artefacts include the following.

Artefact	Purpose
P3O Business Case	Justifies the office model and expected value
P3O Blueprint / Target Operating Model	Describes structure, services, interfaces, and governance
Service Catalogue	Defines what the office provides and to whom
Organisation Structure / Role Profiles	Clarifies reporting lines and responsibilities
Governance Calendar	Schedules boards, reviews, reports, and decision points

Artefact	Purpose
Reporting Pack / Dashboard Suite	Provides portfolio, programme, and project visibility
Standards and Templates Library	Supports consistency in delivery controls
Resource and Capacity Reports	Tracks demand, supply, utilisation, and bottlenecks
RAID / Dependency Consolidation	Escalates enterprise delivery constraints
Benefits Tracking Pack	Supports value and outcome monitoring
Assurance Plan	Coordinates health checks, stage reviews, and governance confidence
Improvement Backlog / Maturity Assessment	Drives evolution of the P3O capability

7.1 Example Document Grouping

7.1.1 Strategic / Enterprise Level

- P3O business case
- target operating model
- service catalogue
- enterprise dashboard pack
- portfolio prioritisation and dependency views
- maturity roadmap

7.1.2 Programme / Delivery Level

- programme office reporting pack
- milestone and dependency maps
- benefits tracking logs
- governance packs and review materials
- integrated RAID summaries

7.1.3 Project / Local Support Level

- local project controls and templates
- schedule administration support
- reporting packs and logs
- configuration and document support
- meeting and board administration

8 RACI Matrix

Below is a practical example RACI for a typical P3O model.

Deliverable / Activity	Executive Sponsor	Head of P3O / EPMO	Portfolio Office	Programme Office	Project Office	Centre of Excellence	PM / PgM
Approve P3O business case	A	R	C	I	I	C	I
Define target operating model	C	A/R	R	C	C	R	C
Define service catalogue	I	A	R	C	C	R	I
Set standards and templates	I	A	C	C	C	R	I
Produce enterprise portfolio dashboard	I	A	R	C	I	C	I
Coordinate programme reporting	I	C	C	A/R	I	I	C
Support project governance admin	I	I	I	C	A/R	I	C

Deliverable / Activity	Executive Sponsor	Head of P3O / EPMO	Portfolio Office	Programme Office	Project Office	Centre of Excellence	PM / PgM
Consolidate RAID / dependencies	I	A	R	R	C	I	C
Coordinate assurance reviews	C	A	R	C	C	R	I
Track benefits at portfolio level	C	A	R	R	I	C	C
Maintain capability and training	I	A	C	I	I	R	I
Run maturity assessment and improvement	I	A	C	C	C	R	I

Legend: R = Responsible, A = Accountable, C = Consulted, I = Informed

---

9 Integration with Other Frameworks

9.1 P3O and COBIT

COBIT provides governance objectives and control expectations. P3O provides the organisational support model that helps operationalise governance across the change portfolio.

- COBIT defines governance requirements.
- P3O helps create the office structure and reporting model to support them.

9.2 P3O and MoP

MoP helps govern **what the portfolio is** and how investment choices are made. P3O helps define **which office capability supports that portfolio**.

- MoP = portfolio decision framework
- P3O = portfolio support operating model

9.3 P3O and MSP

MSP provides programme governance and benefits-led transformation. P3O provides programme office design and support services for those programmes.

9.4 P3O and PRINCE2

PRINCE2 defines project governance and control. P3O helps structure the PMO / project office capability that supports PRINCE2 projects consistently.

9.5 P3O and ITIL 4

ITIL 4 helps with service management and value delivery. P3O helps manage the change governance and office support needed to deliver transformation into live services.

9.6 P3O and TOGAF

TOGAF defines architecture direction and change roadmaps. P3O helps provide the reporting, coordination, and office support structure around the related programmes and projects.

---

10 KPIs and Measures

Typical P3O performance measures include:

KPI	What It Indicates
Portfolio reporting timeliness	Reliability of executive information
Data quality / dashboard accuracy	Confidence in management information

KPI	What It Indicates
Percentage of initiatives using standard controls	Adoption of governance standards
Resource forecast accuracy	Quality of planning and capacity insight
Dependency escalation cycle time	Responsiveness to cross-project constraints
Benefits tracking coverage	Visibility of value realisation
Assurance action closure rate	Effectiveness of follow-up and governance discipline
Stakeholder satisfaction with PMO services	Perceived value of the office model
Reduction in duplicate reporting effort	Efficiency gain from standardisation
PMO maturity score improvement	Capability growth over time

---

11 Benefits

P3O can provide substantial benefits when implemented well:

- clearer enterprise visibility across change initiatives;
- better executive decision support;
- stronger consistency in methods, reporting, and controls;
- improved dependency, resource, and benefits insight;
- more effective assurance and escalation;
- reduced duplication across multiple PMOs;
- stronger capability development and institutional learning; and
- a more strategic PMO / EPMO function.

---

12 Limitations and Risks

P3O also has implementation risks if handled poorly:

- it can become bureaucratic if service value is not clear;
- a central office may be resisted if local autonomy is ignored;
- standardisation can become over-engineering;
- weak sponsorship may leave the office as a reporting factory without influence;
- poor data quality can undermine dashboards and trust; and
- unclear authority boundaries can create tension between office staff and delivery managers.

The strongest implementations focus on **useful services, decision support, and role clarity**, not just administration.

---

13 Practical Use Case

A large organisation has more than 80 concurrent change initiatives. Different business units run local PMOs with different templates, reporting cycles, and status definitions. Executives cannot see total investment exposure, resource conflicts, or strategic dependencies.

A P3O initiative is launched to create:

- a permanent portfolio office for enterprise reporting and prioritisation;
- a centre of excellence for methods, dashboards, and capability support;
- standardised programme office services for strategic transformation programmes; and
- lighter project office support for smaller initiatives.

Within a year, the organisation gains:

- a single executive dashboard for portfolio governance;
- standard milestone, RAID, and dependency views;
- clearer resourcing insight across major programmes;
- consistent governance packs for boards and steering groups; and
- better alignment between strategy, investment decisions, and delivery oversight.

This is where P3O is strongest: not as a local admin function, but as an enterprise **change support architecture**.

---

14 Conclusion

P3O provides a practical framework for designing and governing the support structure around portfolios, programmes, and projects. It helps organisations turn disconnected PMOs into a coordinated operating model that improves visibility, consistency, assurance, and strategic decision support.

In an integrated governance stack:

- **COBIT** helps govern enterprise IT and control expectations;
- **TOGAF** shapes enterprise architecture and transformation roadmaps;

- **ITIL 4** supports service value and operations;
- **PRINCE2** controls projects;
- **MSP** governs programmes;
- **MoP** governs portfolio choice; and
- **P3O** provides the office model that supports all of them.

That makes P3O especially valuable in your governance atlas, because it acts as one of the main bridges between governance design and day-to-day portfolio, programme, and project support.

15 References

- AXELOS. *Portfolio, Programme and Project Offices (P3O)*. AXELOS.
- AXELOS. *P3O Foundation Project Office Certification*. AXELOS.
- AXELOS. *P3O Practitioner Project Office Certification*. AXELOS.
- PeopleCert. *Portfolio, Programme and Project Offices (P3O)*. PeopleCert.
- PeopleCert. *P3O Foundation*. PeopleCert.
- PeopleCert. *P3O Practitioner*. PeopleCert.
- PeopleCert. *Official Training Materials Updates*. PeopleCert.
- Cabinet Office. *Portfolio, Programme and Project Offices (P3O)*. London: TSO / The Stationery Office.
